PES UNIVERSITY

Lab 2 — Agile Backlog Creation & Sprint Simulation in Jira

NAME

N Bhuvan Teja

SRN

PES1UG24CS286

COURSE

Software Engineering · UE24CS341A

SEMESTER & SECTION

5th Semester — E

SECTION 01


Backlog — Epics, User Stories & Story Points

The Lab 1 requirements for this exercise were organised around a student startup crowdfunding platform. Four functional themes became the Epics for this backlog — Campaign Creation & Milestones, Backer Pledging & Rewards, Payment & Fund Release, and Backer Notifications — and twelve User Stories were written under them, each in the As a / I want / So that format and story-pointed on the Fibonacci scale.

Table 1.1 Backlog broken down by Epic, with story points assigned on the Fibonacci scale

Key	User Story	Epic	Points
SSCP-5	Create Campaign	Campaign Creation & Milestones	5
SSCP-6	Define Campaign Milestones	Campaign Creation & Milestones	5
SSCP-7	Browse Campaigns	Backer Pledging & Rewards	3
SSCP-8	Select Reward Tier	Backer Pledging & Rewards	3
SSCP-9	Make a Pledge	Backer Pledging & Rewards	5
SSCP-10	Process Secure Payment	Payment & Fund Release	8
SSCP-11	Submit Milestone Evidence	Payment & Fund Release	5
SSCP-12	Request Fund Tranche	Payment & Fund Release	3
SSCP-13	Review Milestone Evidence	Payment & Fund Release	8
SSCP-14	Release Fund Tranche	Payment & Fund Release	8
SSCP-15	Apply Early-Bird Bonus	Backer Pledging & Rewards	3
SSCP-16	Notify Backers of Fund Release	Backer Notifications	5

Priority followed user impact: the core path of creating a campaign, pledging, paying securely, verifying milestones, and releasing funds was set to High, while the early-bird bonus and backer notifications were set to Medium.

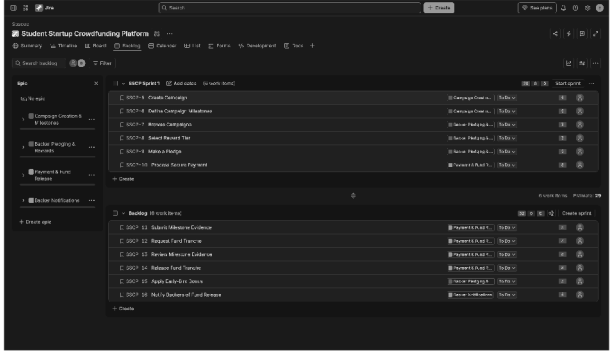


Backlog view with all four Epics, twelve User Stories, and their Fibonacci story points assigned.


SECTION 02

Sprint 1 — Execution


Sprint 1 ran from 3 to 10 September 2026 with a goal of enabling campaign creation and basic backer pledging with secure payment. Six stories carrying 29 story points were pulled into the sprint: Create Campaign, Define Campaign Milestones, Browse Campaigns, Select Reward Tier, Make a Pledge, and Process Secure Payment.




Sprint 1 board shortly after the sprint started, with four stories still To Do.



Sprint 1 board after two stories reached Done and two were In Progress.




Sprint 1 board with four of six stories Done and none left To Do.




Sprint 1 board after all six stories were moved to Done.

Burndown & Completion

All 29 committed story points were burned down within the sprint window, and the sprint was closed with the Complete Sprint action once every item reached Done.

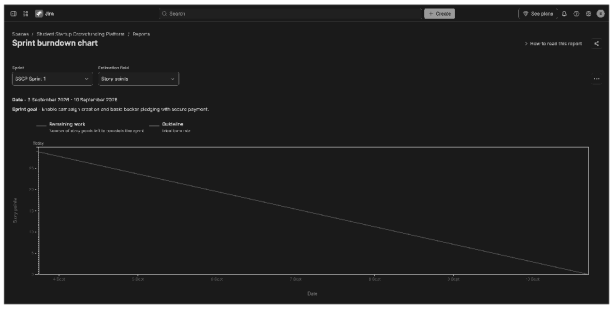

Sprint 1 burndown chart showing remaining work against the ideal guideline.




Completed work items report confirming all six Sprint 1 stories reached Done.


SECTION 03

Sprint 2 — Execution


With Sprint 1 closed, the remaining six stories carrying 32 story points were planned into Sprint 2 (10–17 September), with a goal of completing milestone verification, fund release, and backer notification: Submit Milestone Evidence, Request Fund Tranche, Review Milestone Evidence, Release Fund Tranche, Apply Early-Bird Bonus, and Notify Backers of Fund Release.

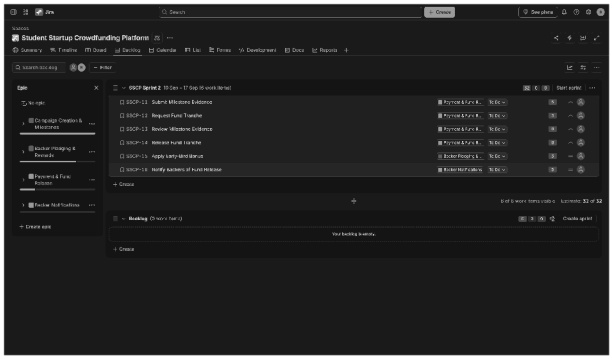


Backlog view after Sprint 1, showing completed Epic progress bars and Sprint 2 populated with the remaining six stories.



Sprint 2 board immediately after the sprint started, all six stories in To Do.



Sprint 2 board midway through, with stories split across To Do, In Progress, and Done.

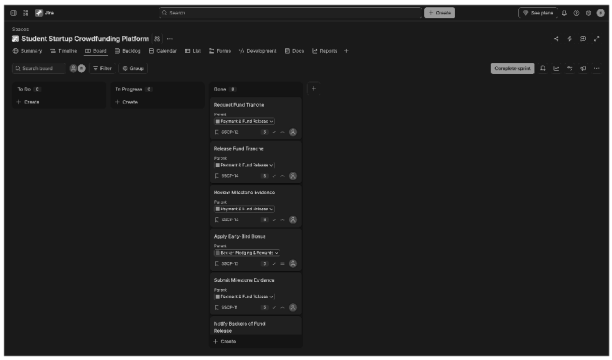


Sprint 2 board after all six stories were moved to Done.

Burndown & Completion

The Sprint 2 burndown tracked all 32 committed points down to zero within the sprint window, and the completed work items report confirms every story reached Done.



Sprint 2 burndown chart showing remaining work against the ideal guideline.



Completed work items report confirming all six Sprint 2 stories reached Done.

SECTION 04

Reflection

Did your estimations reflect the actual effort?

Yes. The story-point estimates gave a reasonable relative picture of effort, complexity, and uncertainty across the backlog. Smaller stories such as Browse Campaigns and Select Reward Tier needed less effort, while higher-point stories such as Process Secure Payment and Review Milestone Evidence carried more complexity and were pointed accordingly.

Was your backlog well-prioritized?

Yes. Core functionality — campaign creation, pledging, secure payment, milestone verification, and fund release — was set to High priority, while enhancement and notification stories such as the early-bird bonus and backer notifications were set to Medium. This followed the handout's instruction to prioritise by user impact and ensured the most important requirements were addressed first.

How did your simulated sprint align with your plan?

Both simulated sprints followed the planned backlog sequence and sprint goals. Stories were progressed from To Do to In Progress to Done as instructed in the handout, and both sprints were closed with every committed story reaching Done.

What insights did the burndown chart give about your team's capacity?

Both burndown charts showed remaining work tracking down to zero against the ideal guideline, confirming that the committed story points for each sprint were achievable within a one-week window. The charts gave a clear visual check on whether the planned workload matched what could realistically be completed in the sprint duration.
